



Name: E.L. Miller Elementary School

Date | Time: 04/12/2024

Project Name/Number: Facility Conditions Improvements / 354-35

Principal: Mr. Mark Bryant

School Contact: Mr. Mark Bryant

Area Superintendent: Ateshia Lester

Project Manager: Ryan Fernandez

Architect: CDH Partners

Contractor: Centennial Contractors

Scope of Work: Major Building Systems Replacement, kitchen equipment replacement, and classroom renovations.

Project Construction Budget: \$7,040,000.00

Project Schedule: *(Timeline with target dates where appropriate)*

- Construction Start – 6/1/2023
- Construction Complete - 8/1/2024

-
- **Previous Quarter Narrative:** Centennial has completed the HVAC renovations for phase 2.

Project Status/Update:

- Centennial has completed the HVAC renovations at the 3rd thru 5th grade hallways.
- Centennial in process of final clean for 3rd thru 5th grade hallways.
- Centennial has completed the test and balance of the HVAC system.

4-Week Look Ahead:

- Centennial has submitted a change proposal for the repaving of the parking lot. This change proposal will be approved at the May Board Meeting.

End



12/28/23 10:12:14 AM EST




1/3/24 12:52:25 PM EST





12/23/23 5:14:58 PM EST

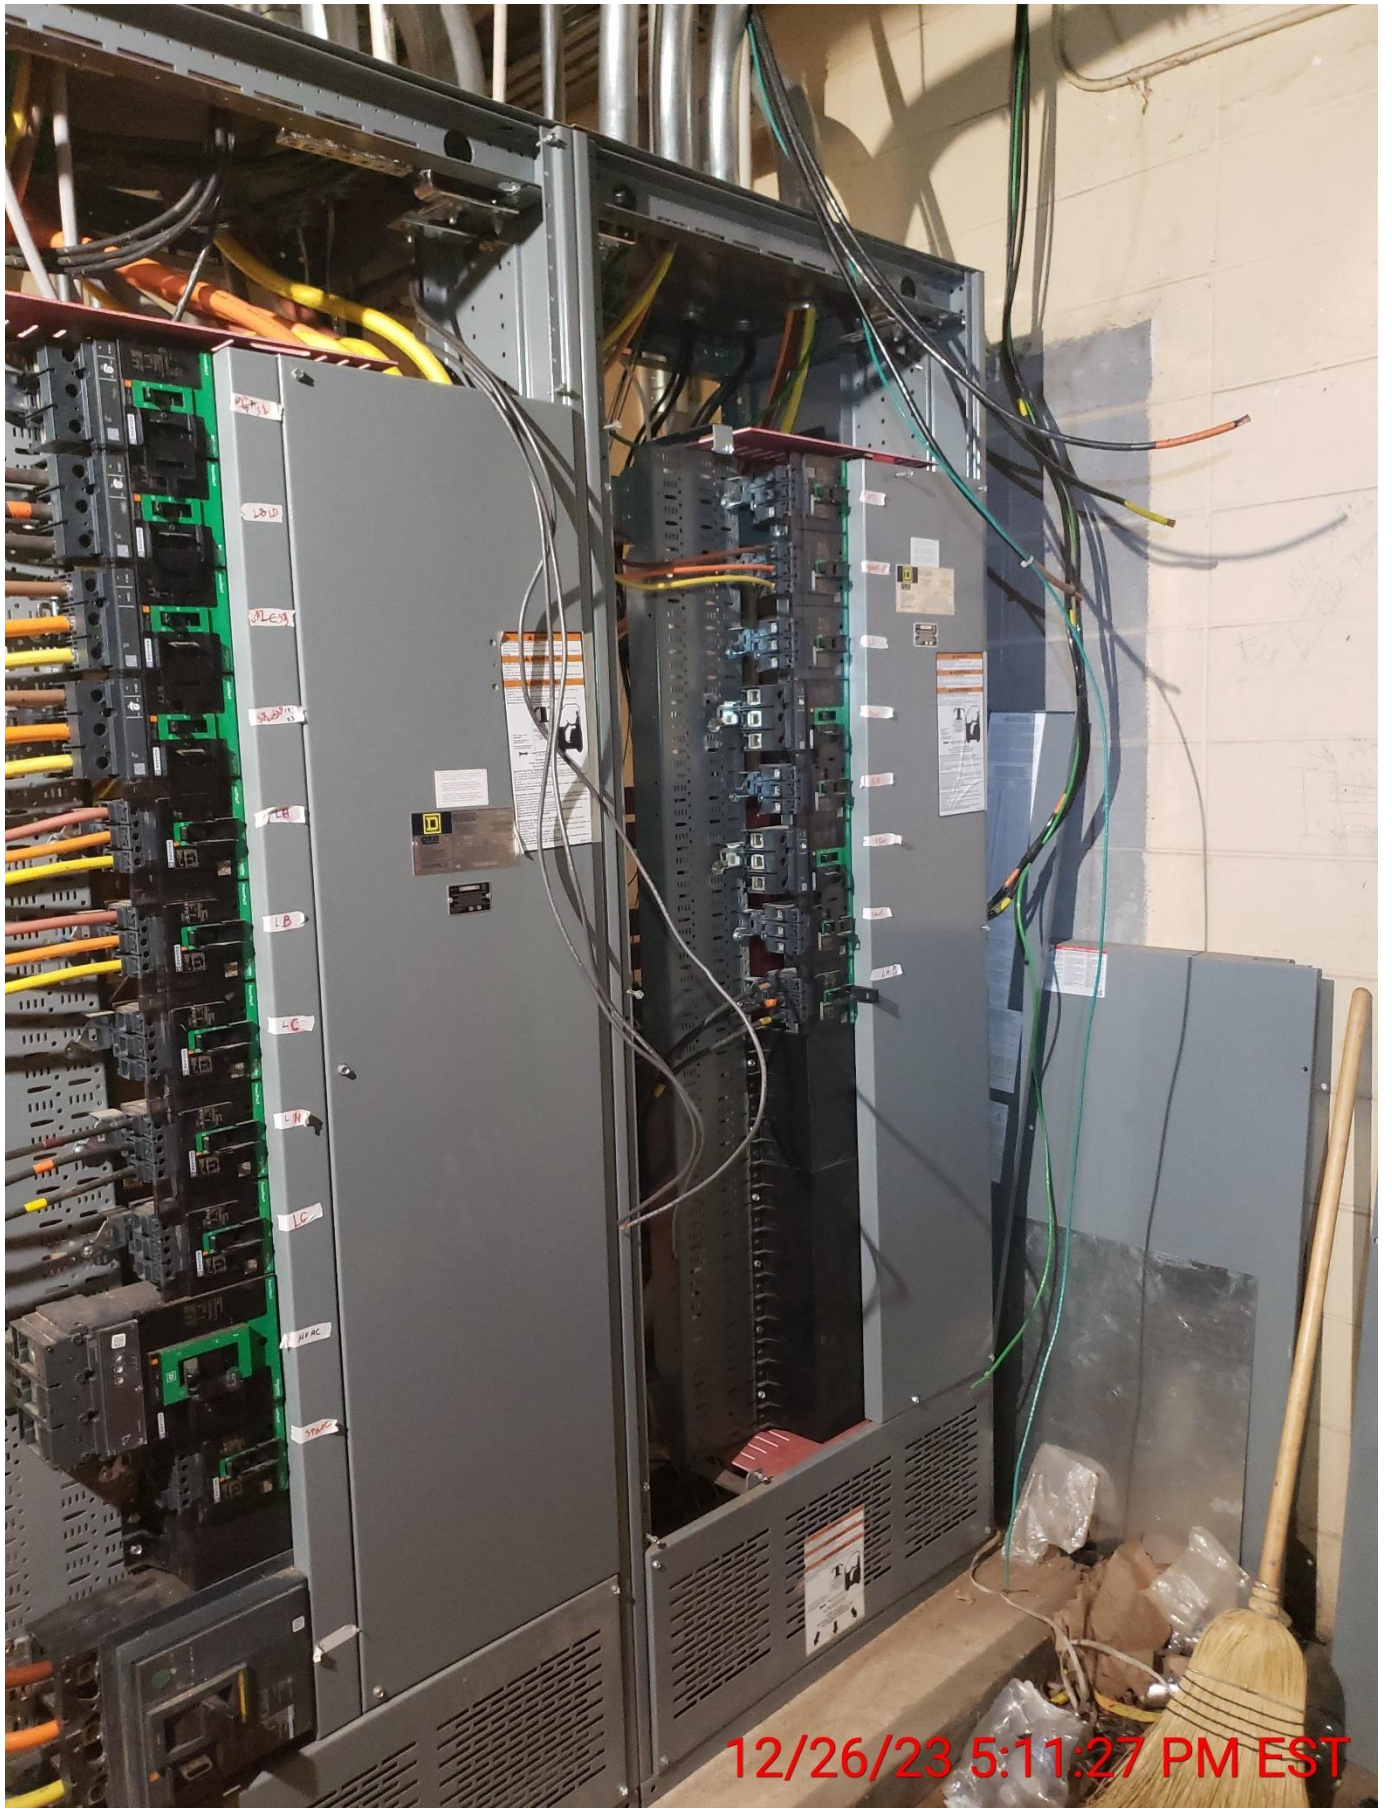

12/26/23 5:11:27 PM EST



12/24/23 12:42:14 PM EST
