



Project Update Report

Report Date	1/10/26
Project Name/Number	Idlewood / 23336
Principal	<i>Robin Elder</i>
School Contact	<i>Robin Elder robin_elder@dekalbschoolsga.org</i>
Regional Superintendent	<i>Dr. Terri Brown</i>
Project Manager	Joseph King
Architect	<i>Cooper Cary & Associates, INC</i>
Contractor	Balfour Beatty

Scope of Work

- HVAC replacement and building renovation
- Sprinkler Installation

Project Construction Budget \$33,054,126

Project Schedule Milestones

- Design Completion - May 2025
- General Contractor Procurement – July 2024
- Construction Start - August 2025
- Construction End – July 2027

Current Project Status:

- Temp walls have been installed
- Overhead weather protection has been installed
- Student transition

4-Week Look Ahead


- Removal of 4 existing trailers
- Shut of power to existing trailers
- Transition of students from inside the school to trailers

End of Project Update Report

Photographs



Caption

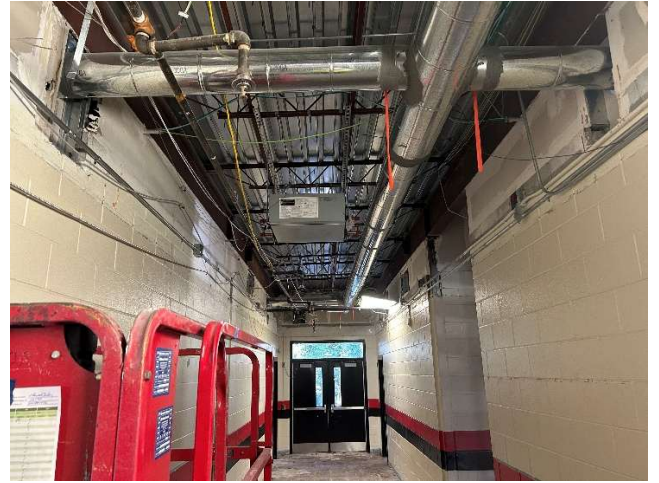

Caption

Caption

Caption
