



# Project Update Report

---

Report Date	2/10/26
Project Name/Number	New Sequoya MS & HS/ 10136
Principal	<i>Tiffany Sims</i>
School Contact	<i>Tiffany Sims tiffany_m_sims@dekalbschoolsga.org</i>
Regional Superintendent	<i>Jacqueline Taylor</i>
Project Manager	Joseph King
Architect	<i>GMC Architects</i>
Contractor	Gilbane

**Scope of Work**

- New construction of Sequoya MS and Sequoya HS

---

**Project Construction Budget** \$235,000,000

---

**Project Schedule Milestones**

- Design Completion - January 2025
- General Contractor Procurement – February 2025
- Construction Start - February 2025
- Construction End – August 2029

---

**Current Project Status:**

- Middle school towers are complete
- Middle school steel is complete
- Middle school decking is complete
- Crane has been located at the site

---


**4-Week Look Ahead**

- Steel to the high school towers
- Fireproofing for steel

---

**End of Project Update Report**

# Photographs

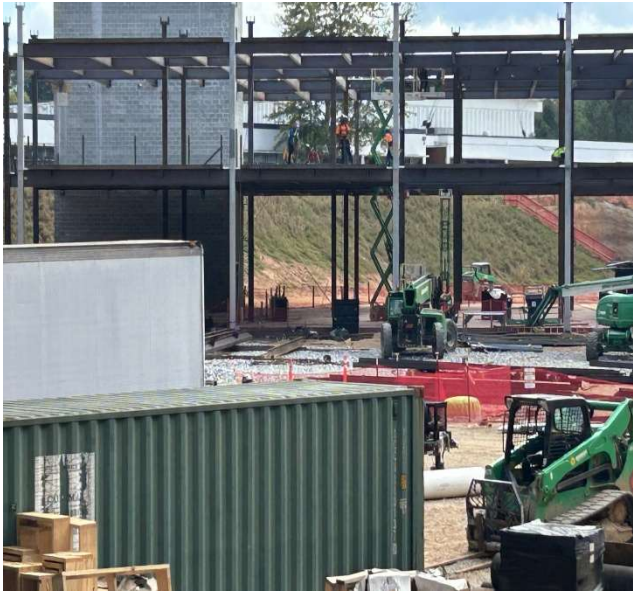

Caption



Caption
